



City of Eagle Point


Robert Miller, Public Works Director/City Engineer

Public Works Update – Stevens Road Improvements September 25, 2019

East Main Street/Stevens Road Improvements

Construction continues for Stage 1 of the E. Main Street/ Stevens Road Improvements by Knife River Materials. Stage 1 will be closed for construction into October of 2019. The detour signs will be revised to state October 30, 2019, however, the detour is anticipated to be open earlier as weather permits.

Access is limited to residents only and to emergency vehicles at all times. A temporary pedestrian detour was placed on Onyx Road, and accessed from Tabor Avenue and Bridgeport Drive on each side.

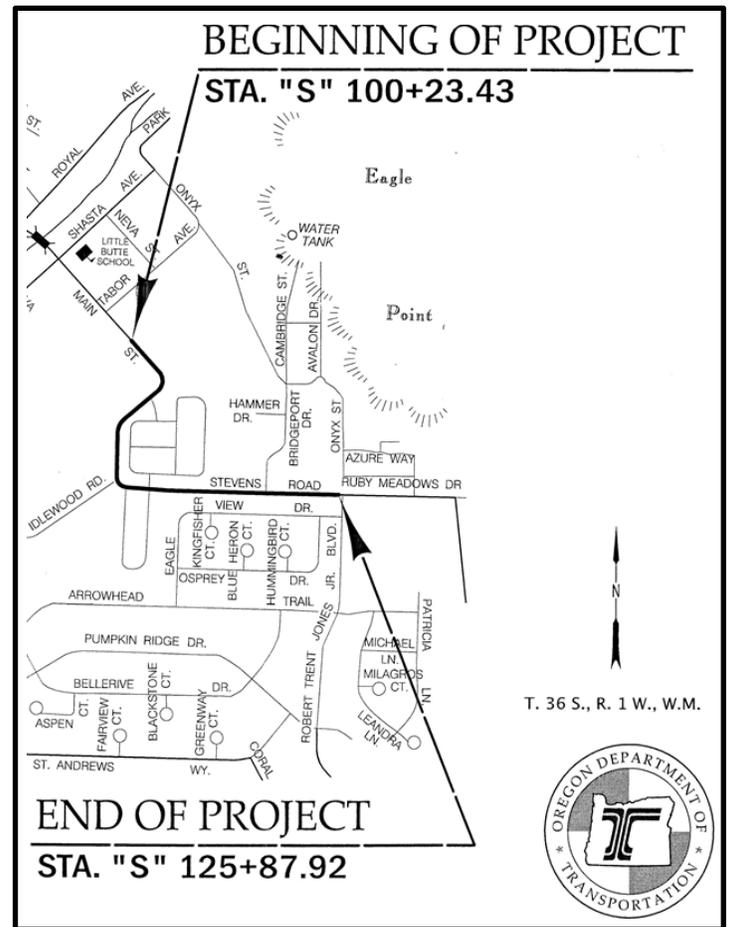

Excavation and placement of the new road base for E. Main Street/Stevens Road.



Visual representation of the completed project.



The road bed is prepared for placement of base and subsequent paving.



The road profile is being revised at the top of the hill to increase sight distance.



The existing storm up the hill was removed for the road widening.



New storm system at Bridgeport Drive.



Storm laterals are in progress.

Construction of the new storm system was completed for Stage 1 and Stage 2. The drainage inlets and laterals are currently being installed.



Erosion control was added.



Onyx Road temporary pedestrian detour.

Two Week Look Ahead

With completion of the retaining walls and storm system, several operations are scheduled for the next two to three weeks (pending good weather):

Stage 1 (Hillside Elementary School to Idlewood Drive)

- Completion of storm inlets - September
- Installation of Water Quality Planters – First week of October
- Installation of conduit for lighting - September
- Curb and Gutter - First week of October
- Light pole foundations - mid October
- Sidewalks/flag holders – mid October

Stage 2 (Idlewood Drive to Robert Trent Jones Boulevard)

- Clearing and tree removal - September
- Completion of storm inlets – September
- Excavation and base – Second week of October

A tentative paving date of October 17, 2019 has been set for the base lift on Stage 1 (pending good weather). Once the first lift of paving has been completed, the road closure detour will be removed. Traffic control (one lane closed) will be required throughout construction. The contract date for completion of the full project is April of 2020. Weather (temperature) will determine when paving and the overall project can be completed.

Public Outreach

Regular updates continue to be sent to the email notification list, and placed on the City's website. Steve Sparkman, Construction Project Manager for OBEC Consulting Engineers, is available to meet onsite with property owners who have specific questions about the project construction.

For project updates please see the City of Eagle Point website, www.cityofeaglepoint.org. For general questions, or to be placed on the email notification list for updates please contact Brigitte at City Hall, (541) 826-4212, brigitte@cityofeaglepoint.org.

