



City of Eagle Point

Robert Miller, Public Works Director/City Engineer


Public Works Update – Stevens Road Improvements

October 19, 2019

East Main Street/Stevens Road Improvements

Construction continues for Stage 1 and Stage 2 of the E. Main Street/ Stevens Road Improvements by Knife River Materials. Stage 1 is scheduled to be closed for construction until October 30, 2019.

Access is limited to residents only and to emergency vehicles at all times. A temporary pedestrian detour was placed on Onyx Road, and accessed from Tabor Avenue and Bridgeport Drive on each side.

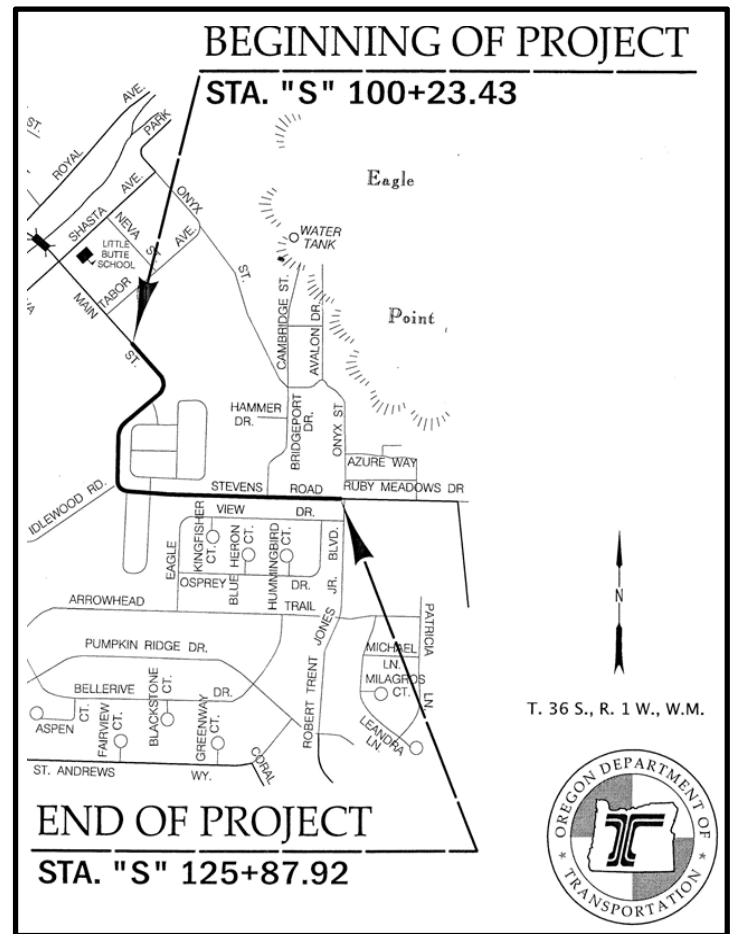

Curb and gutter was completed for Stage 1.









The driveway to the Church on the Hill will be relocated with the project.





Widening for Stage 2 continued (Idlewood Drive to Bridgeport Drive).



Drainage inlets were installed to prepare for paving.



Water quality planter construction.

Two Week Look Ahead

Paving of the base lift of Stage 1 is scheduled for Friday, October 25, 2019. The road will remain closed until October 30 to prepare the project for opening. Construction will continue into November with one-lane traffic control during the day to install light pole foundations and sidewalks/flag holders. The contract date for completion of the full project is April of 2020. Weather will determine when paving and the full project can be completed.

Public Outreach

Regular updates continue to be sent to the email notification list, and placed on the City's website. Steve Sparkman, Construction Project Manager for OBEC Consulting Engineers, is available to meet onsite with property owners who have specific questions about the project construction.

For project updates please see the City of Eagle Point website, www.cityofeaglepoint.org. For general questions, or to be placed on the email notification list for updates please contact Brigitte at City Hall, (541) 826-4212, brigitte@cityofeaglepoint.org.

